


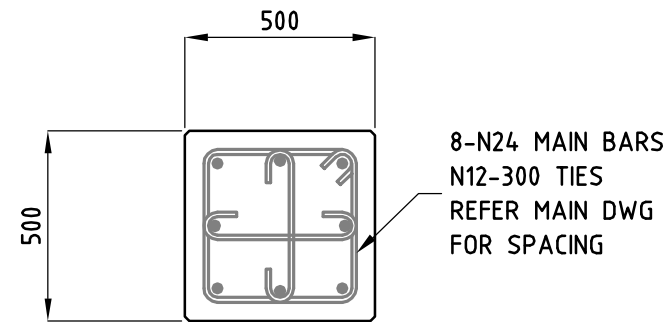
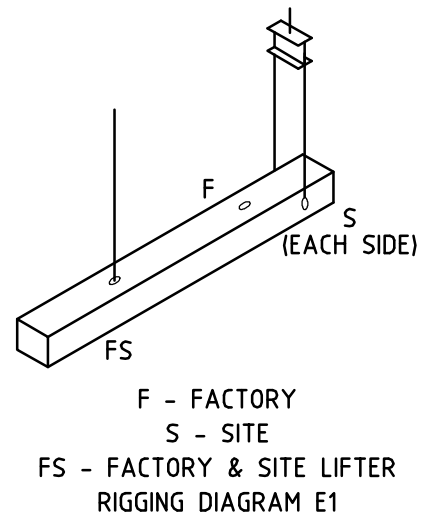


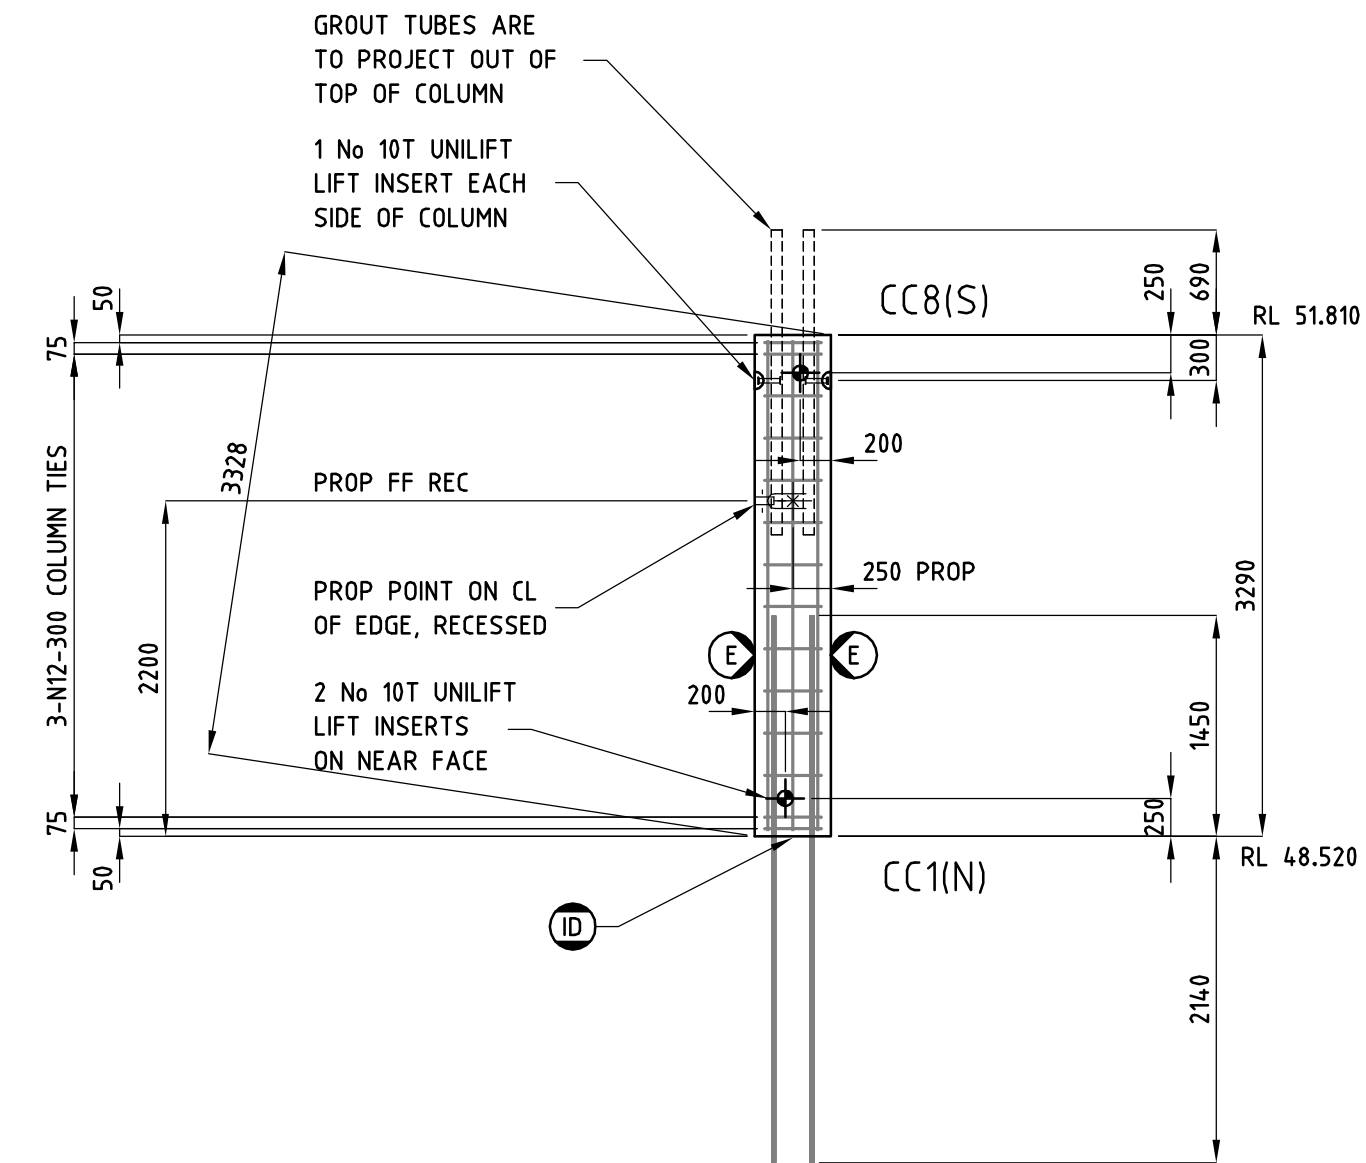

REINFORCEMENT

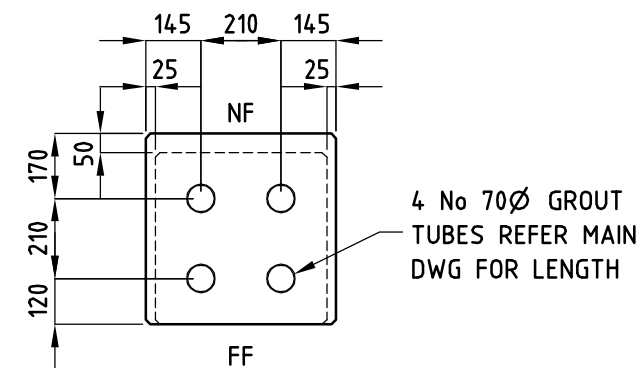

TOP GROUT TUBES

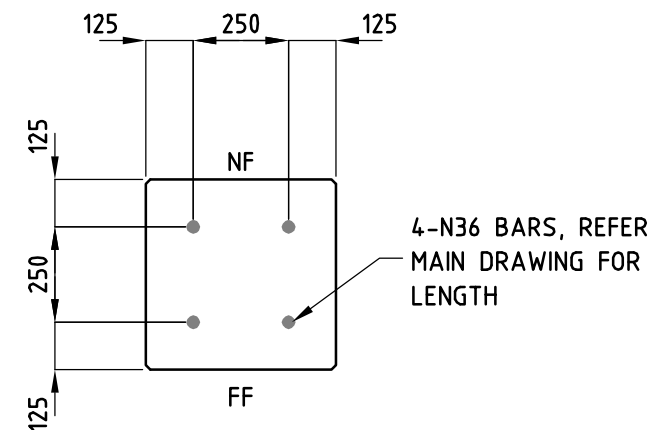

BOTTOM BARS

NOTES:

- COG BARS 400 MM OVERLAP BARS 1000 MM UNO
- PROVIDE 4T LIFT INSERTS (N12 TENSION BAR)
- REV B - RIGGING DIAGRAM REVISED
- RIGGING TO BE APPROVED BY ERECTION ENGINEER

JOB

UNIVERSITY OF MELBOURNE, FACULTY OF ARCHITECTURE

ADVANCED PRECAST (AUST) P/L
TELEPHONE 9706 5111 FAX 9706 4551



DRAWN: 31 JUL 13 GSB
REVISED: 13 AUG 13 GSB

JOB NO 3131
PANEL NO 1P2043
REV B

APPROVED FOR
CONSTRUCTION

THICKNESS	500 MM
NF FINISH	TROWEL
FF FINISH	GOOD TABLE
TYPE	COLUMN
VOLUME	0.82 M ³
GROSS AREA	1.65 M ²
NETT AREA	1.65 M ²
MASS	2.20 T
COG X	250 MM
COG Y	1645 MM
ERECT LEVEL	CURRENT
GRADE AT 28 DAYS	N50
GRADE AT DELIVERY	N20
GRADE AT FACTORY	N10
CONCRETE	NORMAL
MIX	50W-50G (B)
EXTERNAL COVER	35 MM
INTERNAL COVER	35 MM
EDGE CHAMFER	12 MM
DOWEL BARS	NONE

QUALITY ASSURANCE

CONC	SETOUT	REO

ELEVATION B/2

VIEWED LOOKING NORTH

SCALE 1:50

EXT REF
