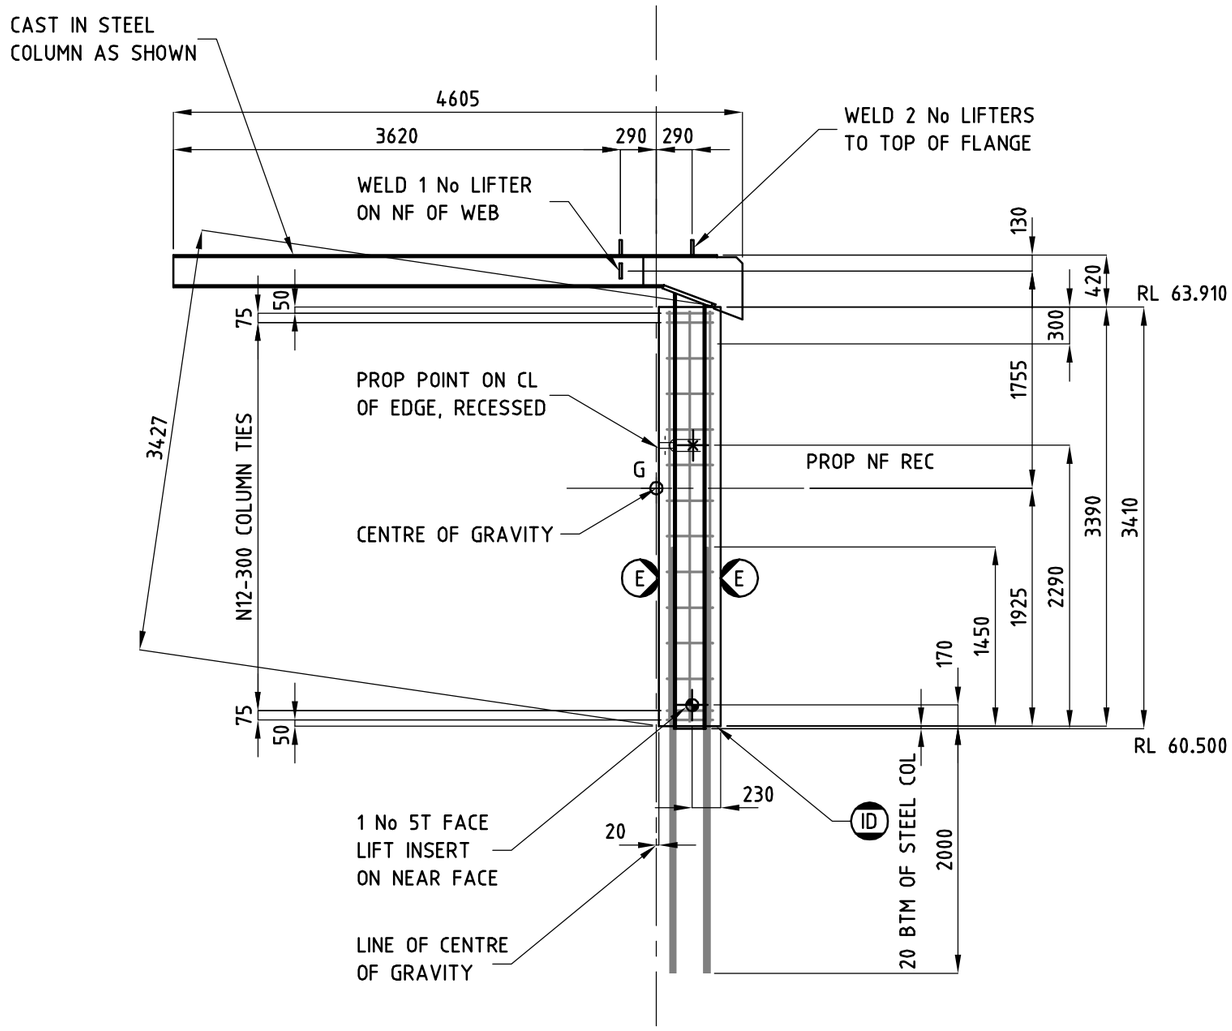

COLUMN CC1
GRIDS A.1/10.1

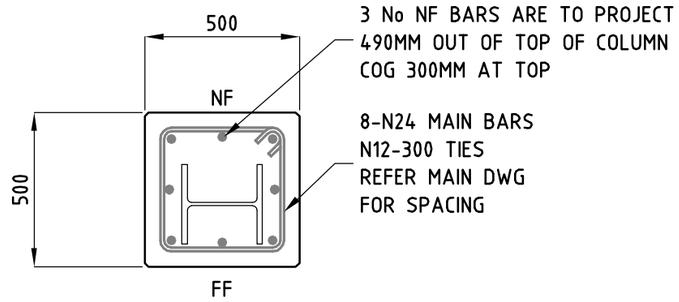

REINFORCEMENT

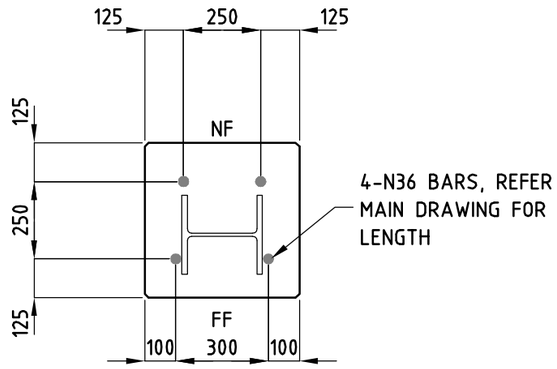

BOTTOM BARS

COG Z = 260MM

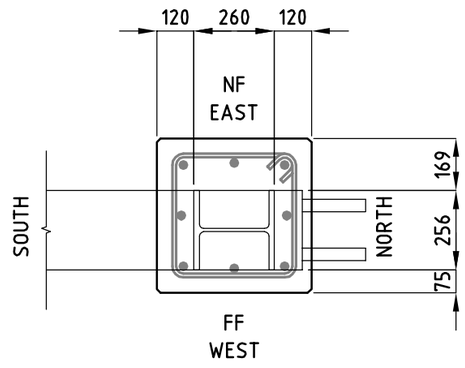

STEEL COLUMN LOCATION



WELD ON LIFTER

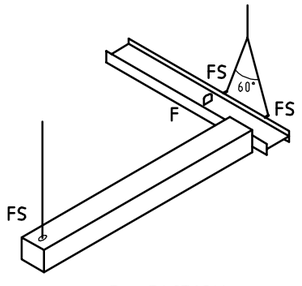

F - FACTORY
S - SITE
FS - FACTORY & SITE LIFTER
RIGGING DIAGRAM S2

NOTES:

- COG BARS 400 MM OVERLAP BARS 1000 MM UNO
- PROVIDE 4T LIFT INSERTS (N12 TENSION BAR)
- REV B - REINFORCEMENT REVISED
- RIGGING TO BE APPROVED BY ERECTION ENGINEER

APPROVED FOR CONSTRUCTION

THICKNESS	500 MM
NF FINISH	TROWEL
FF FINISH	GOOD TABLE
TYPE	COLUMN
VOLUME	0.85 M^3
GROSS AREA	1.69 M^2
NETT AREA	1.69 M^2
MASS	2.89 T
COG X	-20 MM
COG Y	1925 MM
ERECT LEVEL	CURRENT
GRADE AT 28 DAYS	N50
GRADE AT DELIVERY	N20
GRADE AT FACTORY	N10
CONCRETE	NORMAL
MIX	50W-50G [B]
EXTERNAL COVER	35 MM
INTERNAL COVER	35 MM
EDGE CHAMFER	12 MM
DOWEL BARS	NONE

QUALITY ASSURANCE

CONC	SETOUT	REO

ELEVATION	A.1/10.1
VIEWED	LOOKING WEST
SCALE	1:50
EXT REF	

JOB
UNIVERSITY OF MELBOURNE, FACULTY OF ARCHITECTURE

DRAWN:	14 AUG 13	SV
REVISED:	10 OCT 13	GSB

ADVANCED PRECAST (AUST) P/L
TELEPHONE 9706 5111 FAX 9706 4551

JOB NO	PANEL NO	REV
3131	4P2015	B
